


1 There are VAV's serving both base bid and alternate offices. Please clarify how we are to price. Same with transfer ducts. See below for an example:

a. The VAV replacement, supply ductwork and transfer ductwork is in the base bid, the ceiling work in rooms 210.10 and 210.6 in this example are in the base bid due to the need to remove the ceiling to install the VAV, ceilings in Alt#1 may remain, with new diffusers and grilles.

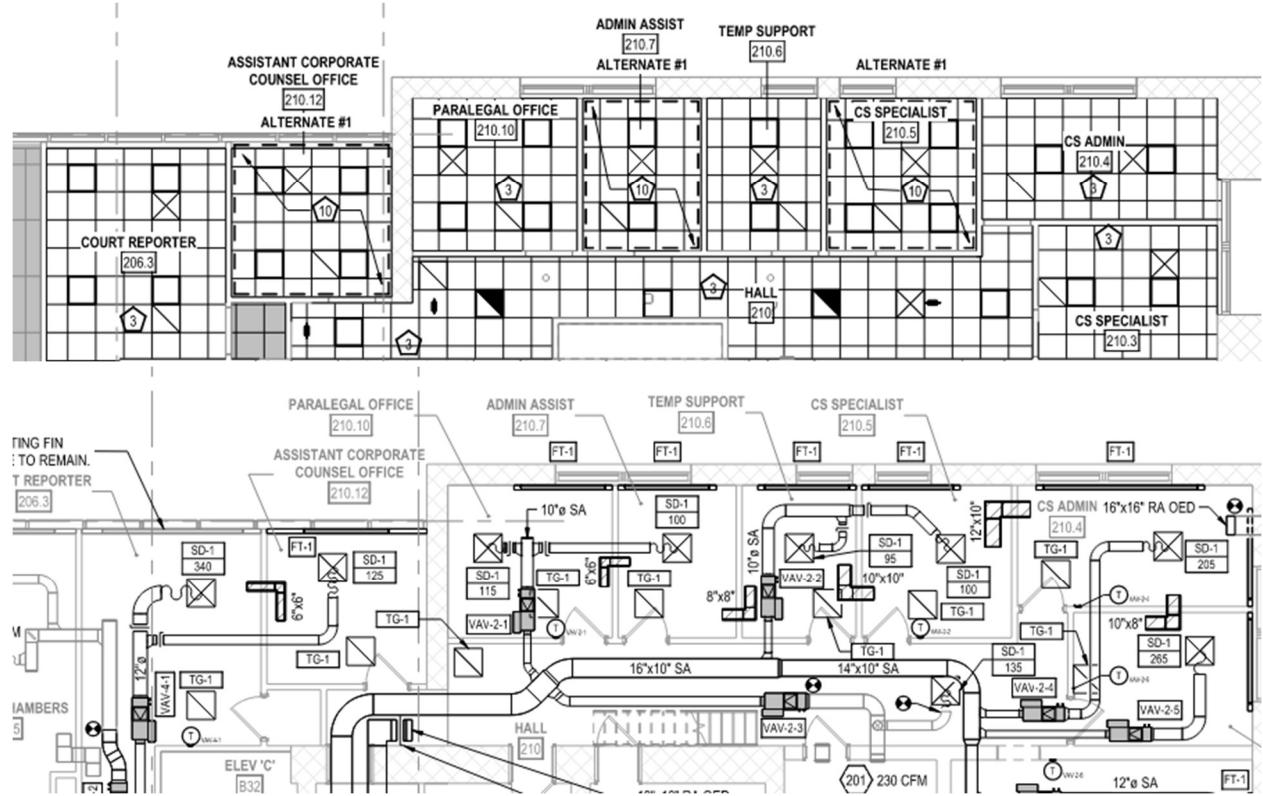

2 23 05 23 – Can we use valves with soldered/ProPress ends to match installed piping system. Specs indicate threaded ends

a. Soldered and ProPress for copper tubing is acceptable.

3 Please confirm for equipment indicated to have controls valves replaced, all other associated valves and piping components will be reused.

a. Where control valves are installed on existing equipment, only the TCV is included in the scope. Where existing branch lines are used to feed new coils or equipment, all components shall be new except for the isolation valves.

4 Can we locate shut off valves for finned tube on floor below their location?

Isolation valves may be located on the floor below for up feed perimeter heat, where the ceiling below is accessible.
